


Educational Data Integration Weekly Meeting
MT Office of Public Instruction and PowerSchool

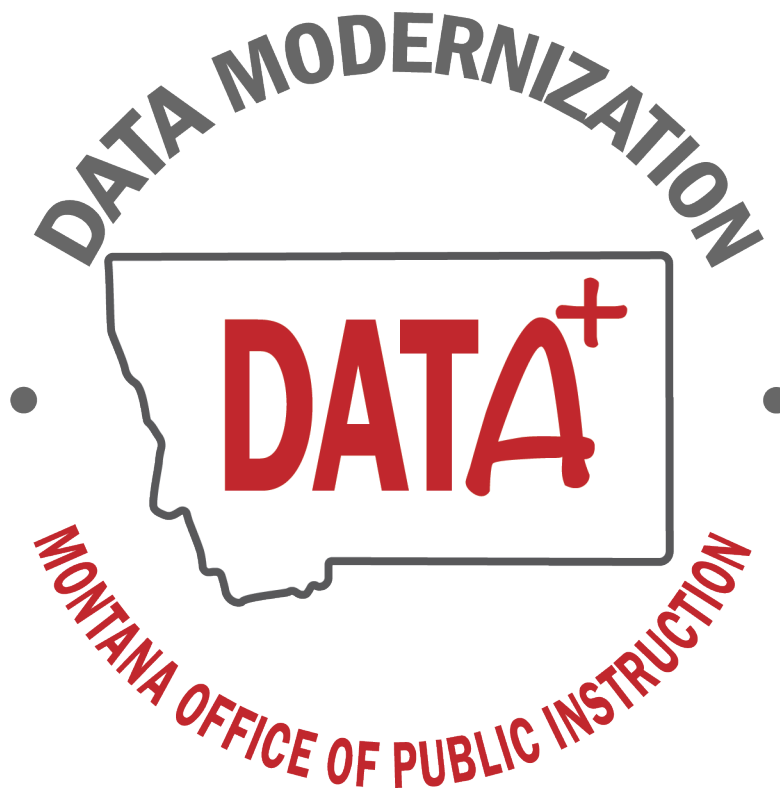


Meeting Date: February 1, 2024

Materials:

Meeting Attendance

Meeting Agenda

Meeting Summary



OPI Data Modernization Project

Weekly Meeting with PowerSchool Summary

Date: February 1, 2024

Attendees:			
<input checked="" type="checkbox"/> Chris Sinrud, OPI	<input checked="" type="checkbox"/> Andy Campbell, OPI	<input checked="" type="checkbox"/> Ashley Perez, OPI	<input checked="" type="checkbox"/> Melissa Straw, PS
<input checked="" type="checkbox"/> Kevin Benson, PS	<input checked="" type="checkbox"/> Robert King, PS	<input checked="" type="checkbox"/> Anna Hoerner, OPI	<input checked="" type="checkbox"/> Steve Ciarrocchi, PS
<input type="checkbox"/> Edward Dedic, PS	<input checked="" type="checkbox"/> Sarah Singer, PS	<input type="checkbox"/> Rob Stutz, OPI	<input checked="" type="checkbox"/> Syed Ali, PS

Agenda Items:	<ol style="list-style-type: none"> 1. Data Dictionary 2. Connected Intelligence: <ul style="list-style-type: none"> PowerSchool Student Information System Connections Status - Custom Connector Update - VPN Discussion Update Infinite Campus Student Information System Connection Update Status 3. OCM Updates 4. Other Project Updates 																																			
General Updates:	Continuing to make progress on the data dictionary. Will also look to get a process for adding to the data dictionary post-deployment if there are changes/additions.																																			
Connected Intelligence:	The team continues to work on the analysis and mapping. Also continuing to work on replicating data from iC into CI.																																			
Unified Insights:	Pending completion of other tasks. There was a demo for key staff at OPI, and the product is available for other demos as needed.																																			
Project Governance:	Future milestone. No current updates.																																			
Milestones:	<table border="1"> <thead> <tr> <th>Milestone</th> <th>Project Status</th> <th>Planned Completion</th> <th>Current Forecast</th> <th>Actual Date</th> </tr> </thead> <tbody> <tr> <td>1: Draft Assessment Output</td> <td>Completed</td> <td>9/8/2023</td> <td>9/8/2023</td> <td>9/8/2023</td> </tr> <tr> <td>2: MT Review and Feedback</td> <td>Completed</td> <td>9/15/2023</td> <td>9/18/2023</td> <td>9/18/2023</td> </tr> <tr> <td>3: Final Approval</td> <td>Completed</td> <td>9/22/2023</td> <td>9/22/2023</td> <td>9/22/2023</td> </tr> <tr> <td>4a: Connected Intelligence w/ 2 sources</td> <td>In Progress</td> <td>10/20/2023</td> <td>7/20/2024</td> <td></td> </tr> <tr> <td>4b: Replication w/ 6 additional sources</td> <td>Not Started</td> <td>7/20/2025</td> <td>7/20/2025</td> <td></td> </tr> <tr> <td>5a: Base Unified Insights Modules Deployed</td> <td>Not Started</td> <td>8/20/2024</td> <td>8/20/2024</td> <td></td> </tr> </tbody> </table>	Milestone	Project Status	Planned Completion	Current Forecast	Actual Date	1: Draft Assessment Output	Completed	9/8/2023	9/8/2023	9/8/2023	2: MT Review and Feedback	Completed	9/15/2023	9/18/2023	9/18/2023	3: Final Approval	Completed	9/22/2023	9/22/2023	9/22/2023	4a: Connected Intelligence w/ 2 sources	In Progress	10/20/2023	7/20/2024		4b: Replication w/ 6 additional sources	Not Started	7/20/2025	7/20/2025		5a: Base Unified Insights Modules Deployed	Not Started	8/20/2024	8/20/2024	
Milestone	Project Status	Planned Completion	Current Forecast	Actual Date																																
1: Draft Assessment Output	Completed	9/8/2023	9/8/2023	9/8/2023																																
2: MT Review and Feedback	Completed	9/15/2023	9/18/2023	9/18/2023																																
3: Final Approval	Completed	9/22/2023	9/22/2023	9/22/2023																																
4a: Connected Intelligence w/ 2 sources	In Progress	10/20/2023	7/20/2024																																	
4b: Replication w/ 6 additional sources	Not Started	7/20/2025	7/20/2025																																	
5a: Base Unified Insights Modules Deployed	Not Started	8/20/2024	8/20/2024																																	

	5b: Unified Insights Customizations Complete	Not Started	7/20/2025	7/20/2025
	6: Post-Deployment Assessment	Not Started	6/20/2025	6/20/2025
	7: Solution Acceptance and Sign-off	Not Started	7/20/2025	7/20/2025
