


Educational Data Integration Weekly Meeting
MT Office of Public Instruction and PowerSchool

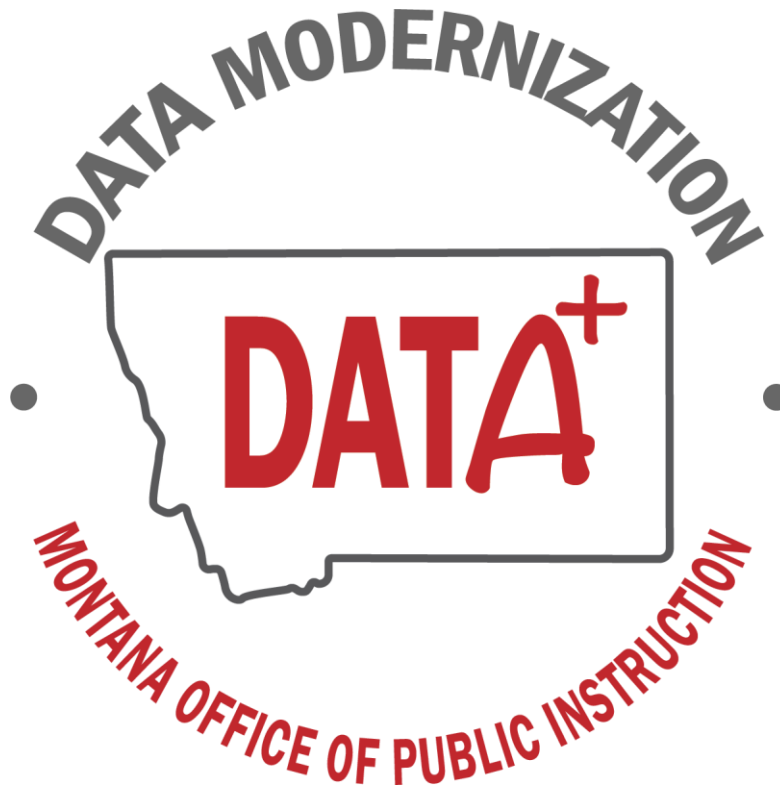


Meeting Date: February 23, 2024

Materials:

Meeting Attendance

Meeting Agenda

Meeting Summary



OPI Data Modernization Project

Weekly Meeting with PowerSchool Summary

Date: February 23, 2024

Attendees:			
<input type="checkbox"/> Chris Sinrud, OPI	<input checked="" type="checkbox"/> Andy Campbell, OPI	<input checked="" type="checkbox"/> Ashley Perez, OPI	<input checked="" type="checkbox"/> Melissa Straw, PS
<input checked="" type="checkbox"/> Kevin Benson, PS	<input checked="" type="checkbox"/> Robert King, PS	<input type="checkbox"/> Anna Hoerner, OPI	<input checked="" type="checkbox"/> Steve Ciarrocchi, PS
<input checked="" type="checkbox"/> Edward Dedic, PS	<input checked="" type="checkbox"/> Sarah Singer, PS	<input type="checkbox"/> Rob Stutz, OPI	<input type="checkbox"/> Jamey Erath, OPI

Agenda Items:	<ol style="list-style-type: none"> 1. General Updates 2. Connected Intelligence Update 3. Unified Insights Update 4. Other project information 																																			
Topic:	Discussion:																																			
General Updates	PowerSchool is reviewing feedback from OPI on the VPNs that are supposed to be set up. There are several upcoming meetings to review upcoming aspects of the project outside of the weekly check-in.																																			
Connected Intelligence	Additional users have been set up with access to CI. A User Management Consultation will be scheduled for a future date, and conversations will be starting regarding data replication. The custom connector analysis is scheduled to start again the week of 3/4.																																			
Data Dictionary	This has been completed.																																			
Unified Insights	This step has been moved to In Progress. Discussions have started within PowerSchool to determine next steps. A technical deep dive is scheduled on 2/29 to review the next steps for UI.																																			
Project Governance	Future milestone; no updates.																																			
Milestones:	<table border="1"> <thead> <tr> <th>Milestone</th> <th>Project Status</th> <th>Planned Completion</th> <th>Current Forecast</th> <th>Actual Date</th> </tr> </thead> <tbody> <tr> <td>1: Draft Assessment Output</td> <td>Completed</td> <td>9/8/2023</td> <td>9/8/2023</td> <td>9/8/2023</td> </tr> <tr> <td>2: MT Review and Feedback</td> <td>Completed</td> <td>9/15/2023</td> <td>9/18/2023</td> <td>9/18/2023</td> </tr> <tr> <td>3: Final Approval</td> <td>Completed</td> <td>9/22/2023</td> <td>9/22/2023</td> <td>9/22/2023</td> </tr> <tr> <td>4a: Connected Intelligence w/ 2 sources</td> <td>In Progress</td> <td>10/20/2023</td> <td>7/20/2024</td> <td></td> </tr> <tr> <td>4b: Replication w/ 6 additional sources</td> <td>Not Started</td> <td>7/20/2025</td> <td>7/20/2025</td> <td></td> </tr> <tr> <td>5a: Base Unified Insights Modules Deployed</td> <td>In Progress</td> <td>8/20/2024</td> <td>03/2025</td> <td></td> </tr> </tbody> </table>	Milestone	Project Status	Planned Completion	Current Forecast	Actual Date	1: Draft Assessment Output	Completed	9/8/2023	9/8/2023	9/8/2023	2: MT Review and Feedback	Completed	9/15/2023	9/18/2023	9/18/2023	3: Final Approval	Completed	9/22/2023	9/22/2023	9/22/2023	4a: Connected Intelligence w/ 2 sources	In Progress	10/20/2023	7/20/2024		4b: Replication w/ 6 additional sources	Not Started	7/20/2025	7/20/2025		5a: Base Unified Insights Modules Deployed	In Progress	8/20/2024	03/2025	
Milestone	Project Status	Planned Completion	Current Forecast	Actual Date																																
1: Draft Assessment Output	Completed	9/8/2023	9/8/2023	9/8/2023																																
2: MT Review and Feedback	Completed	9/15/2023	9/18/2023	9/18/2023																																
3: Final Approval	Completed	9/22/2023	9/22/2023	9/22/2023																																
4a: Connected Intelligence w/ 2 sources	In Progress	10/20/2023	7/20/2024																																	
4b: Replication w/ 6 additional sources	Not Started	7/20/2025	7/20/2025																																	
5a: Base Unified Insights Modules Deployed	In Progress	8/20/2024	03/2025																																	

	5b: Unified Insights Customizations Complete	Not Started	7/20/2025	7/20/2025
	6: Post-Deployment Assessment	Not Started	6/20/2025	6/20/2025
	7: Solution Acceptance and Sign-off	Not Started	7/20/2025	7/20/2025
