


Educational Data Integration Weekly Meeting
MT Office of Public Instruction and PowerSchool

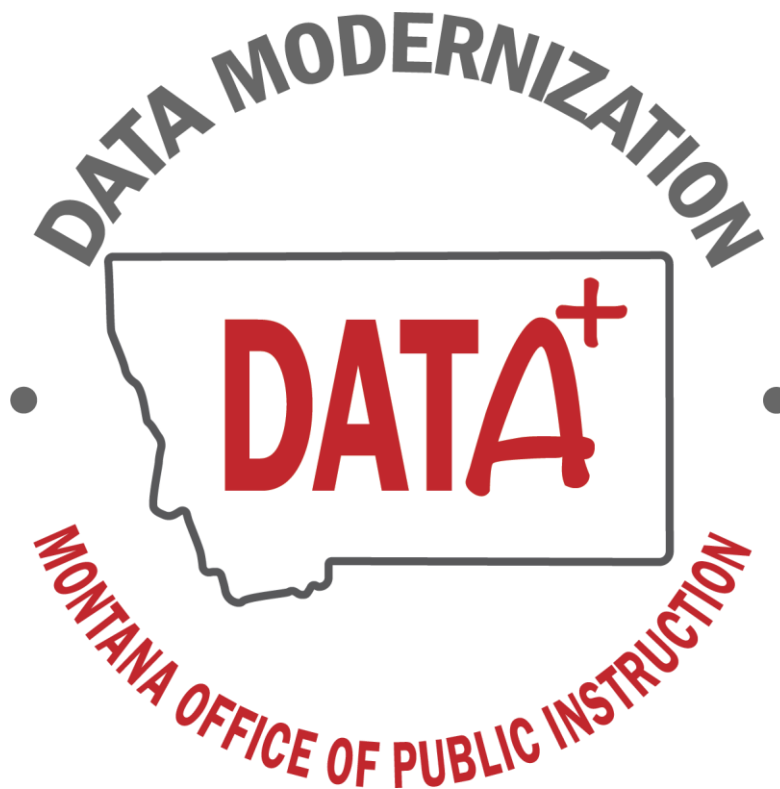


Meeting Date: April 11, 2024

Materials:

Meeting Attendance

Meeting Agenda

Meeting Summary



OPI Data Modernization Project

Weekly Meeting with PowerSchool Summary

Date: April 11, 2024

Attendees:			
<input type="checkbox"/> Chris Sinrud, OPI	<input checked="" type="checkbox"/> Andy Campbell, OPI	<input checked="" type="checkbox"/> Ashley Perez, OPI	<input checked="" type="checkbox"/> Melissa Straw, PS
<input type="checkbox"/> Kevin Benson, PS	<input checked="" type="checkbox"/> Robert King, PS	<input checked="" type="checkbox"/> Anna Hoerner, OPI	<input checked="" type="checkbox"/> Steve Ciarrocchi, PS
<input checked="" type="checkbox"/> Edward Dedic, PS	<input checked="" type="checkbox"/> Sarah Singer, PS	<input type="checkbox"/> Rob Stutz, OPI	<input checked="" type="checkbox"/> Jamey Erath, OPI
<input checked="" type="checkbox"/> Chad Sears, PS	<input checked="" type="checkbox"/> Chris Bushnell, OPI		

Agenda Items:	<ol style="list-style-type: none"> 1. General Updates 2. Connected Intelligence Update 3. Unified Insights Update 4. Other project information 																									
Topic:	Discussion:																									
General Updates	The project team got the JIRA demo and met to discuss the communications plan. OPI is scheduled to attend a PS Compliance Usergroup session. Roadmap updates are in progress to align on back-to-school scope and timelines.																									
Connected Intelligence	The Data Unloading Session was completed on 4/11. PowerSchool received the information needed to move forward with scheduling ongoing replication for the iC replication.																									
Unified Insights	PowerSchool is making progress on UI implementation. PS and OPI are working together to determine the scope and timelines for back-to-school and what is possible. The mapping and gap analysis have been completed. The custom connector is being updated to load data. The UI implementation plan has been created, and follow-up calls will be scheduled to provide more detailed information on the plan. The Risk Analysis and Student Readiness modules are currently undergoing analysis.																									
Project Governance	Future milestone, no updates.																									
Milestones:	<table border="1"> <thead> <tr> <th>Milestone</th> <th>Project Status</th> <th>Planned Completion</th> <th>Current Forecast</th> <th>Actual Date</th> </tr> </thead> <tbody> <tr> <td>1: Draft Assessment Output</td> <td>Completed</td> <td>9/8/2023</td> <td>9/8/2023</td> <td>9/8/2023</td> </tr> <tr> <td>2: MT Review and Feedback</td> <td>Completed</td> <td>9/15/2023</td> <td>9/18/2023</td> <td>9/18/2023</td> </tr> <tr> <td>3: Final Approval</td> <td>Completed</td> <td>9/22/2023</td> <td>9/22/2023</td> <td>9/22/2023</td> </tr> <tr> <td>4a: Connected Intelligence w/ 2 sources</td> <td>In Progress</td> <td>10/20/2023</td> <td>7/20/2024</td> <td></td> </tr> </tbody> </table>	Milestone	Project Status	Planned Completion	Current Forecast	Actual Date	1: Draft Assessment Output	Completed	9/8/2023	9/8/2023	9/8/2023	2: MT Review and Feedback	Completed	9/15/2023	9/18/2023	9/18/2023	3: Final Approval	Completed	9/22/2023	9/22/2023	9/22/2023	4a: Connected Intelligence w/ 2 sources	In Progress	10/20/2023	7/20/2024	
Milestone	Project Status	Planned Completion	Current Forecast	Actual Date																						
1: Draft Assessment Output	Completed	9/8/2023	9/8/2023	9/8/2023																						
2: MT Review and Feedback	Completed	9/15/2023	9/18/2023	9/18/2023																						
3: Final Approval	Completed	9/22/2023	9/22/2023	9/22/2023																						
4a: Connected Intelligence w/ 2 sources	In Progress	10/20/2023	7/20/2024																							

	4b: Replication w/ 6 additional sources	Not Started	7/20/2025	7/20/2025
	5a: Base Unified Insights Modules Deployed	In Progress	8/20/2024	3/2025
	5b: Unified Insights Customizations Complete	Not Started	7/20/2025	7/20/2025
	6: Post-Deployment Assessment	Not Started	6/20/2025	6/20/2025
	7: Solution Acceptance and Sign-off	Not Started	7/20/2025	7/20/2025
